


RESERVOIRS 1 AND 2 PUMP STATION UPGRADES PROJECT

January 22, 2025

Reservoir 1 – Site Layout

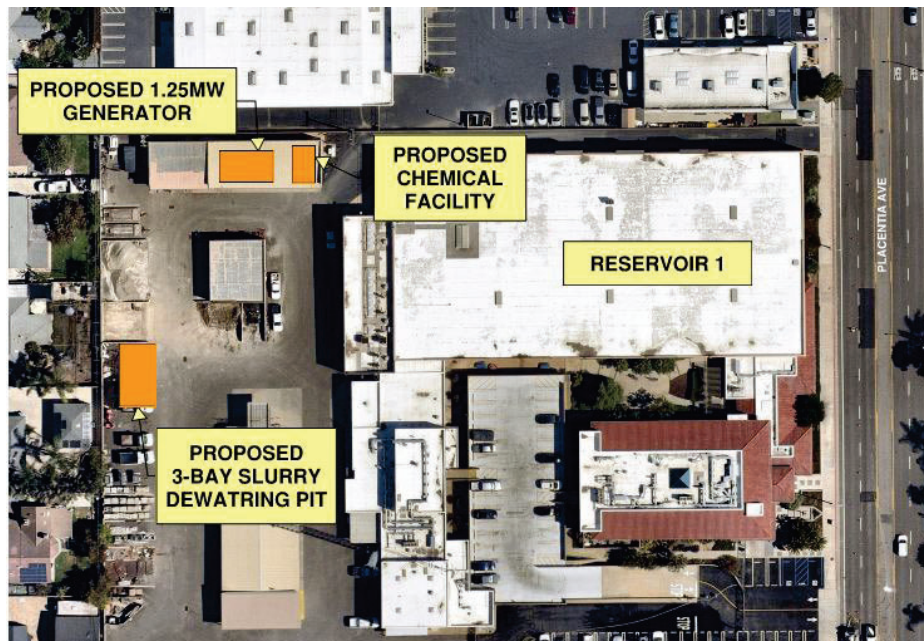

Reservoir 1 - Construction



3 | January 22, 2025



Reservoir 1 - Construction



4 | January 22, 2025




Reservoir 1 - Construction



5 | January 22, 2025



Reservoir 2 – Site Layout

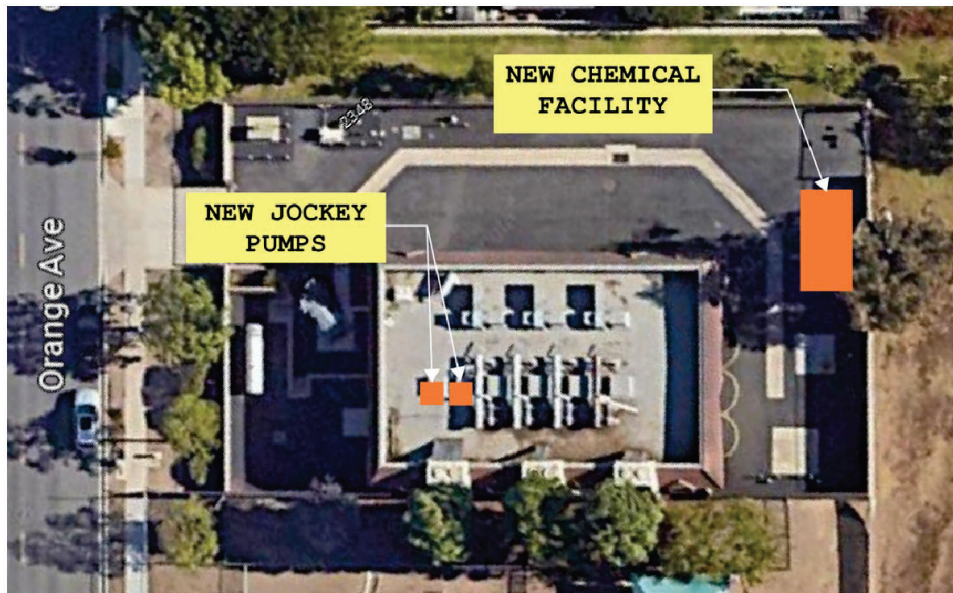

6 | January 22, 2025



Reservoir 2 - Construction



7 | January 22, 2025



Reservoir 2 - Construction



8 | January 22, 2025



Reservoir 2 - Construction



9 | January 22, 2025




Reservoir Project Schedule

Task	2024				2025				2026	
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Submittals and Procurement	█	█								
Reservoir 2			█	█	█					
Reservoir 1				█	█	█	█	█	█	
Project Closeout									█	█

10 | January 22, 2025



Reservoir Project Planned vs. Actual

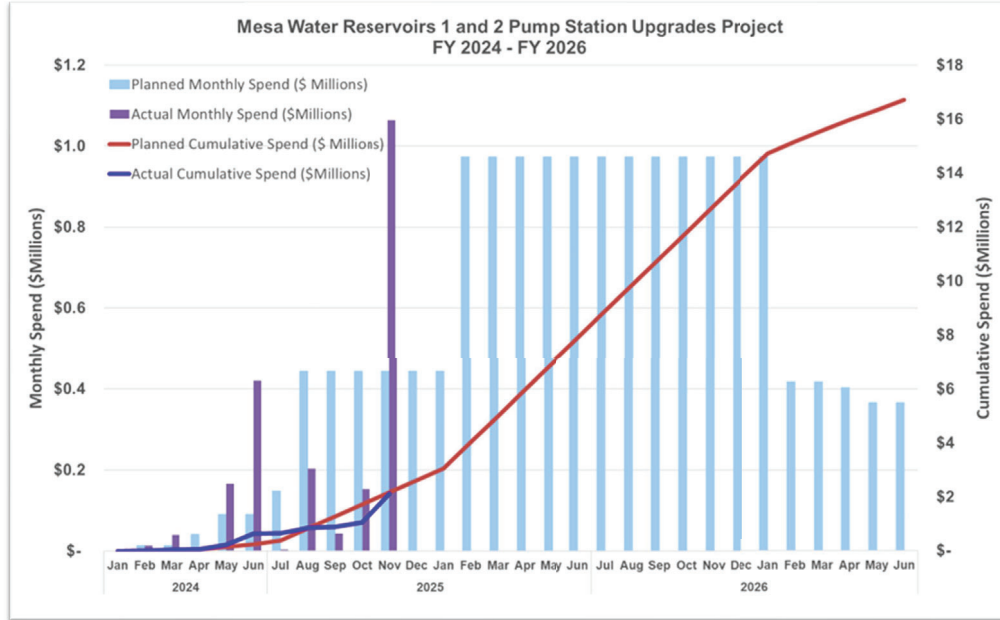

11 | January 22, 2025



QUESTIONS?
